

GRANGER

ADVANCE THE ART OF BUILDING

2020

BOND

CHARLOTTE PUBLIC SCHOOLS

CONSTRUCTION
UPDATE

June 2022



Tennis Courts, Concession Building & ALC



Completed Since Last Update:

- Punch List Items – At Concessions
- Tennis Court Fencing Punch Walk
- Tennis Court Punchlist Items

Work In Progress:

- ALC Scope Completion
- ALC Remaining Punchlist

Upcoming work:

- Civil Punch List Walk For All Phase I Sites Will Take Place During ALC Civil Punch Walk
- Fence & Bollard Installation
- Asphalt Repair and Reseeding at the Tennis Court Path



Phase II – CHS Sitework, Additions & Renovations



Completed Since Last Update:


- Building Pad Set
- Most Underground Utilities set
- Foundation Layout
- Retention Pond Construction
- Kitchen & Breakroom Demo

Work In Progress:

- Building Façade Demolition
- Building Footing Excavation
- Underground Utility Completion
- Kitchen & Breakroom Work
- New Kitchen Duct Work

Upcoming work:

- Foundation Ground Stabilization using Piers
- Excavation Completion & Foundation Concrete
- Parking Lot Work

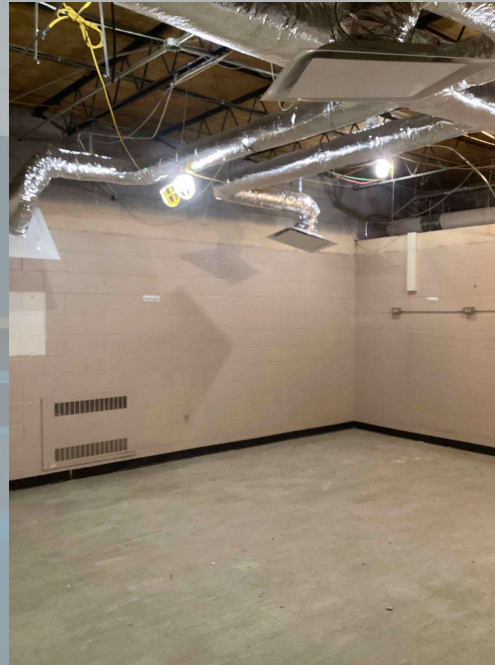

Phase II – GES Sitework, Additions & Renovations



Completed Since Last Update:

- Broke ground on the work
- Sight clearing
- Demolition of Existing Parking Lot & Drives
- Storm Water Utilities
- Building Pad complete



Work In Progress:

- Gas Line Relocation
- Building Footing Excavation
- Fiber Line (Internet) Relocation
- Building Tie-In Point Demolition

Upcoming work:

- Excavation & Foundation Concrete
- Parking Lot Work
- Sanitary Line Tie-In
- Block Foundation Wall



WELCOME TO
CHARLOTTE
HIGH SCHOOL

Phase II – WES Sitework, Additions & Renovations



Completed Since Last Update:

- Broke ground on the work
- Sight clearing
- Building Pad complete

Work In Progress:

- Parking Lot Milling
- Building Tie-In Point Demolition
- Retention Pond Tie-In

Upcoming work:

- Building Footing Excavation
- Parking Lot Work
- Sanitary & Storm Line Tie-In
- Block Foundation Wall



Phase II – WECC Sitework



Completed Since Last Update:

- Parking Lot and Entrance Concrete Demolition

Work In Progress:

- Site Demolition

Upcoming work:

- New Asphalt Paving & Striping
- Concrete Paving



Phase II – Service Center Sitework



Completed Since Last Update:

- Collar Extension of Parking Lot Structures

Work In Progress:

- Site Preparation
- Parking Area Millings Distribution

Upcoming work:

- Parking Area Millings Work Completion

