

Tennis Courts & Concession Building

Work In Progress

- Tennis Fence Installation
- Tennis Coatings (Prep Work)
- Final Grading and Seeding
- Final Roof Framing in the Concession Building
- Roof Installation – Concession Building
- Mechanical, Electrical, and Plumbing Rough-In – Concession Building
- Light Pole Installation



Concession Building, Framing and Roofing Nearly Complete

Upcoming Work

- Tennis Coating Completion
- Installation of Tennis Nets
- Concession Building Rough-In Inspections
- Concession Building – Hang and Finish Drywall Ceiling.
- Install Doors on the Concession Building



Concession Building, Site Graded Ready for Seeding



Tennis Fence Fabric is Being Installed



Site Concrete is Nearly Complete

Anticipated Completion: Tennis Courts 9/20/21, Concession Building 10/21

Weymouth ECC Center Renovation

Work In Progress


- Framing (Complete)
- Mechanical, Electrical, and Plumbing Rough-in (Complete)
- Rough-In Inspections Complete
- Hang and Finish Drywall
- Replace IT Room A/C Unit (Complete)
- New Lighting Installed in The Kitchen (Complete)
- New Door Hardware at Secure Entry

Upcoming Work

- Painting
- Casework and Countertop Installation
- Flooring Installation
- Doors and Door Hardware Installation



New Closet Created in Classroom 100 as Part of The Secure Entry reconfiguration

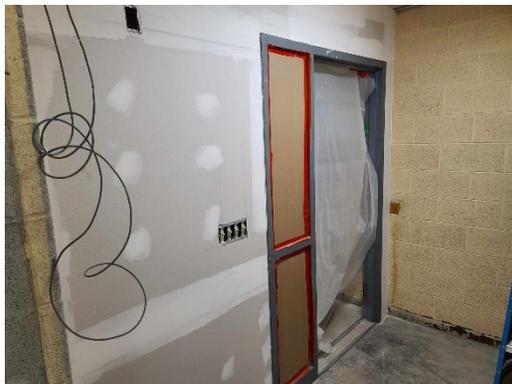

New Entry in Classroom 100 in former Storage Closet



New Wall in The Kitchen to House the New Double Oven

Anticipated Completion: 10/1/21

Agricultural Learning Center

Work In Progress

- Building Demolition
- Site Grading

Upcoming Work

- Footing Excavation
- Concrete Footing Installation
- Building Framing



Existing Agricultural Building Being Demoed



Site Cleared for New Agricultural Learning Center Building

Anticipated Completion: 12/2021
